



REGIONALSAN

TAKING THE WASTE OUT OF WATER

Sacramento Regional County Sanitation District

Secondary Sedimentation Tanks No. 1 & 13 Repair Project

RFB No. 8244

Pre-Bid Meeting and Site Tour

June 8, 2017

Agenda

- Introductions
- SST No.1 & 13 Repair Overview
- Contract Documents and Contract Requirements
- Site Visit Logistics

Introductions

- Scott Jones – Project Manager
- Tambi Stewart – Issuing Officer
- Aaron Bihlman – Project Engineer
- Lucy Escobar – Senior Civil Engineer


SST No. 1 & 13 Repair Overview

- Description of Work
- Work Restrictions/Coordination
- Project Milestones/Liquidated Damages

SST No. 1 & 13 Repair Work

Work Elements includes:

- ✓ Modifying beam support brackets
- ✓ Replacing top bearing pads; adding new bottom bearing pads
- ✓ Releveling the weirs on SST No. 1

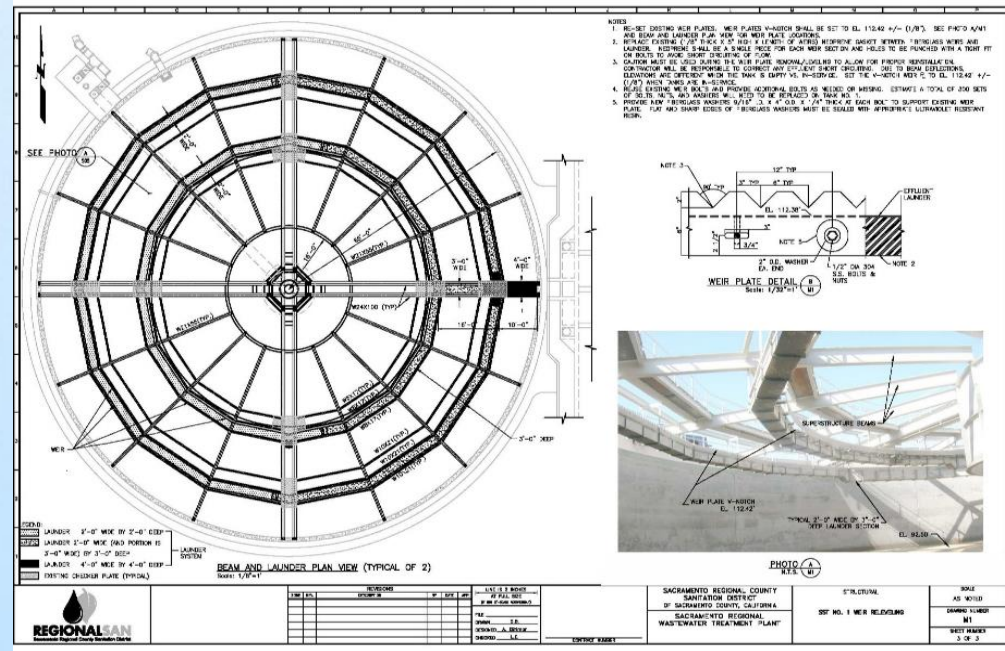

Work Restrictions/Coordination

- Activities that affect the existing plant, operations, and other concurrent contractor work will require coordination between Regional San and Contractors.
- Concurrent Project Construction
 - Return Activated Sludge (RAS) Project
 - WRH & WRL Pipeline Project

Work Restrictions

Item Number	Description of Work	Cross Reference
1	SST No. 13 repair work	--
2	SST No. 1 repair work; testing and leveling	A,B

Requirement Number	Requirement	Cross Reference
A	SST. No. 1 repair work: EchoWater RAS Project Contractor must be complete with SST Battery 1 work (SST's No 1-8) before work can begin on SST. No. 1	2
B	SST No. 13 repair work: SST No. 13 repair work shall be completed before repair work can begin on SST No. 1	--

** Regional San reserves the right to modify the sequence of work*

Insurance Requirements


- The insurance provisions attached on Appendix A must be complied with by you if awarded the order
- Proof of insurance must be provided to Regional San prior to commencement of work

Prevailing Wages

- Pursuant to Section 1770, and following, of the California Labor Code, the Contractor shall pay not less than the *prevailing rate* of per diem wages as determined by the Director of the California Department of Industrial Relations.
- Copies of the prevailing rate of per diem wages are on file at the office of the Sacramento County Labor Compliance Section.

Site Access/Security

- Site Access to SSTs thru Dwight Road Security Gate
 - From Laguna Blvd
- Security
 - All staff will be badged

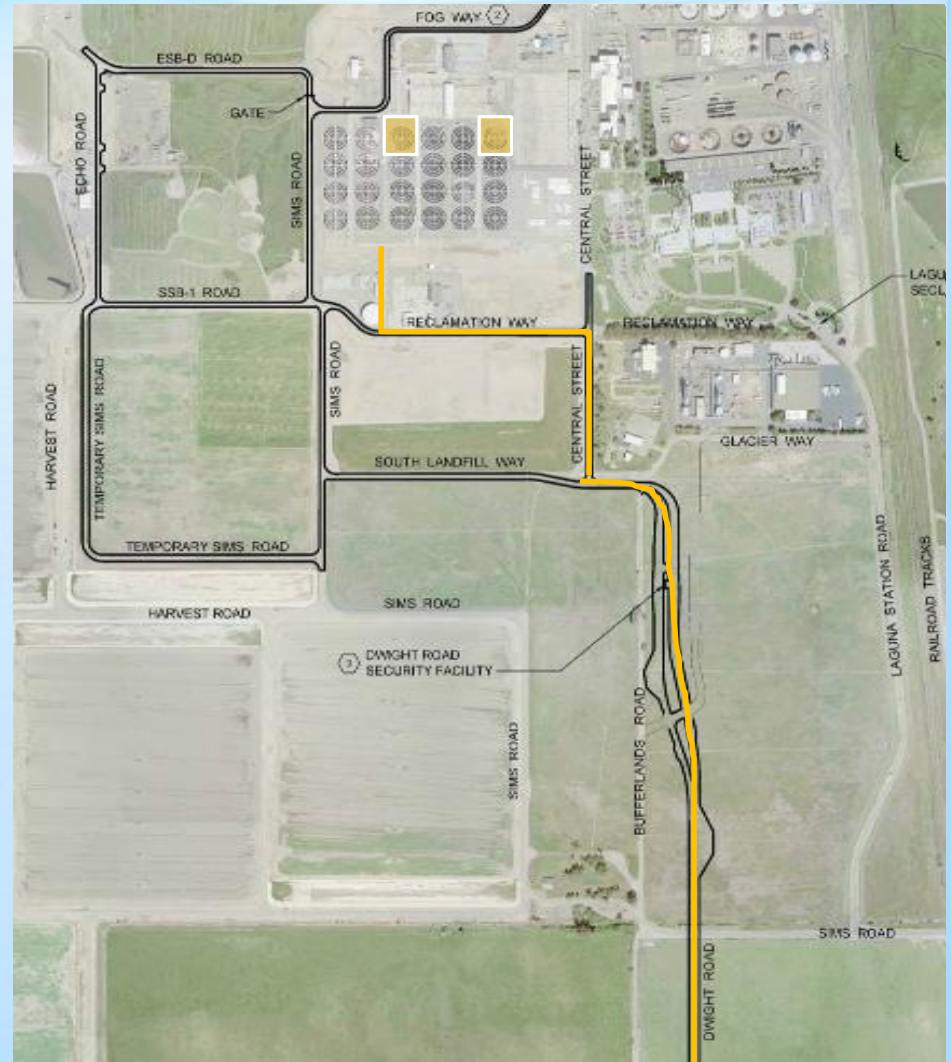

Bidding Requirements

- Forms required when submitting bid:
 - Cover Page with authorized signature
 - Regarding Insurance Coverage (See Appendix B)
 - Instruction for Bid Security and Bid Guaranty Bond (See Appendix E)
 - Instruction for Performance Bond (See Appendix G)
 - Instruction for Payment Bond (See Appendix H)
 - Cost Response (See Appendix I)
 - Contractor Experience Statement (See Appendix J)
 - Proposed Subcontractors Form (See Appendix K)
 - Exception to Bid / Response Page (See Appendix L)
 - Contractor License Certification (See Appendix M)
 - Noncollusion Declaration (See Appendix N)
 - Two (2) copies of the bid and mark the original as the “Original” or “Master Copy”

NTP Schedule

- Bid Due – June 21, 2017 at 3:00 PM
- Intent to Award – June 26, 2017
- Insurance and Bond Vetted – July 11, 2017
- Award Contract – July 12, 2017
- Contractor NTP – July 13, 2017 (anticipated)
- District Access Requests

Site Visit Logistics

- ✓ Site tour is mandatory for General Contractors as part of pre-bid meeting participation.
- ✓ Questions are encouraged to be submitted in writing. If you have a question and want a response, email jonessc@sacsewer.com
- ✓ The deadline to submit questions is June 14th, 2017.

Walking tour to SST No. 1 & 13

- ✓ Review SST No. 1
- ✓ Review SST No. 13
- ✓ Point out ongoing work of EchoWater-RAS contractor

Site Visit Logistics



Questions?
